



Banedanmark's Network Statement 2025 – Appendix 3.5A

Appendix 3.5A

Contents	Page
1. Long-distance lines	
Overview of the Long-distance lines	4 - 6
TIB 1 – 35	8 – 20
2. S-Lines	
Overview of the S-Lines	7
TIB 810 – 880	21 – 22

Fjernbanen TIB 23 - 26

Netredegørelse 2025 - overblik 2025

- (Børkop) - Fredericia
Vejadgang til DSB værksted
- (Hørning) - Aarhus / (Brabrand) - Aarhus
Ombygning Aarhus H
- Frederikshavn – Sindal
Sporformyelse Kvissel
- Tinglev - Padborg
Vedligehold



Fjernbanen TIB 29 - 35

Netredefølge 2025 - overblik 2025


- Esbjerg - (Lunderskov)
Bramming – Tønder
Esbjerg - Spangsbjerg
Ibrugtagning af Signalprogrammet
- (Holstebro) - (Vemb)
(Holstebro) - (Skjern)
(Vemb) - (Skjern)
(Aulum) - Holstebro
Sporfornyelse Skjern – Holstebro
- Holstebro + Skjern
Etablering af ladestandere
- (Funder) – (Silkeborg)
Afvanding
- (Funder) – (Engesvang)
Dæmningsudbedring



S-banen

Netredegørelse 2025 - overblik 2025

- Svanemøllen - Hillerød
Spor- og broarbejde
- (Ballerup) – Veksø
Stiunderføring
- (Bispebjerg) - Fuglebakken
Renovation af Nørrebro St

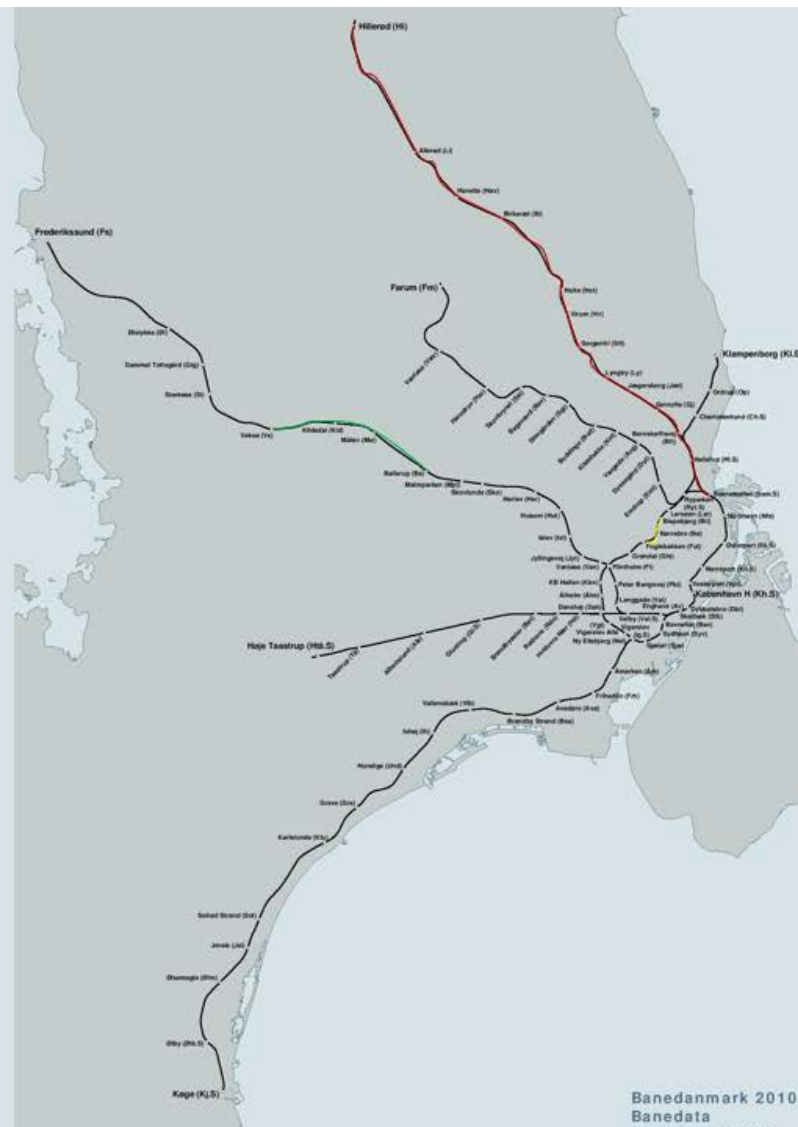

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
1	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	5 days and 12 hours		23.03 - 29.03 Stage 0	1. main track Høje Taastrup - Roskilde possessed	Banedanmark	High
2	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 3, 4 and 5	10 days		29.03 - 07.04 Stage 1a	Track 3, 4, and 5 possessed. 3. and 4. main track Høje Taastrup – Roskilde possessed	Banedanmark	High
3	1	(Høje Taastrup) – (Roskilde)	Track renewal Høje Taastrup-Roskilde	Bridge works bridge 15232 Hedehusene Hovedgaden	21 days		29.03 - 19.04	3. and 4. main track Høje Taastrup – Roskilde possessed	Banedanmark	High
4	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 3, 4 and 5	39 days		07.04 - 15.05 Stage 1b	Track 4 and 5 possessed. 3. and 4. main track Høje Taastrup – Roskilde possessed	Banedanmark	High
5	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 2 and 3	40 days		15.05 - 23.06 Stage 2	Track 2 and 3 possessed. 2. and 3. main track Høje Taastrup – Roskilde possessed. access to track 0 to/from Roskilde only to/from 1. main track	Banedanmark	High
6	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	4 days		23.05 - 26.05 Stage 2a	Track 1 possessed. 1. main track Høje Taastrup - Roskilde possessed, access to/from track 0 only in Glostrup end of the station	Banedanmark	High
7	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	4 days		30.05 - 02.06 Stage 2a	Track 1 possessed. 1. main track Høje Taastrup - Roskilde possessed, Access to/from track 0 only in Glostrup end of the station	Banedanmark	High

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
8	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	4 days		06.06 - 09.06 Stage 2a	Track 1 possessed. 1. main track Høje Taastrup - Roskilde possessed, access to/from track 0 only in Glostrup end of the station	Banedanmark	High
9	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	4 days		13.06 - 16.06 Stage 2a	Track 1 possessed. 1. main track Høje Taastrup – Roskilde possessed, Access to/from track 0 only in Glostrup end of the station	Banedanmark	High
10	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1	4 days		13.06 - 16.06 Stage 2b	Track 1 possessed. 1. main track Høje Taastrup – Roskilde possessed.	Banedanmark	High
11	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1 and 2	6 days		07.07 - 12.07 Stage 3a	Track 1 Possessed Track 2 possessed. 2. main track Høje Taastrup - Roskilde possessed. Access to intermodal terminal not affected.	Banedanmark	High
12	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 0, 1 and 2	16 days		12.07 - 21.07 Stage 3b	Track 0, 1 and 2 possessed. 1. and 2. main track Høje Taastrup - Roskilde possessed. No access to intermodal terminal during the period.	Banedanmark	High
13	1	Høje Taastrup – (Roskilde)	Track renewal Høje Taastrup	Track works Høje Taastrup Station Track 1 and 2	35 days		21.07 - 31.08 Stage 3c	Track 1 and 2 possessed. 1. and 2. main track Høje Taastrup - Roskilde possessed.	Banedanmark	High
14	1	(Høje Taastrup) – (Roskilde)	Track renewal Høje Taastrup-Roskilde	Bridge works bridge15232 Hedehusene Hovedgaden	21 days		07.07 - 28.07	1. and 2. main track Høje Taastrup - Roskilde possessed	Banedanmark	High

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
15	1	Borup - Kværkeby	Roskilde – Ringsted residual works	Mechanical reconstruction of tracks by an RPM-machine	8 days and 8 hours		11.04 at 22:00 – 20.04 at 04:00	Single track operations	Banedanmark	High
16	1	Kværkeby - Borup	Roskilde – Ringsted residual works	Mechanical reconstruction of tracks by an RPM-machine	5 days		20.04 at 04:00 – 25.04 at 04:00	Single track operations	Banedanmark	High
17	1	Viby - Roskilde	Roskilde – Ringsted residual works	Mechanical reconstruction of tracks by an RPM-machine	7 days		25.04 at 04:00 – 01.05 at 04:00	Single track operations	Banedanmark	High
18	1	Roskilde - Viby	Roskilde – Ringsted residual works	Mechanical reconstruction of tracks by an RPM-machine	5 days		01.05 at 04:00 – 06.05 at 04:00	Single track operations	Banedanmark	High
19	1	Viby - Borup	Roskilde – Ringsted residual works	Mechanical reconstruction of tracks by an RPM-machine	4 days		06.05 at 04:00 – 10.05 at 04:00	Single track operations	Banedanmark	High
20	1	Sorø – (Slagelse)	NFSP0542 Ringsted – Slagelse Speed upgrade and track renewal	Preparation for mounting of a new switch in Sorø	5 days and 8 hours		16.04 at 20:00 – 22.04 at 04:00	Single track operations	Banedanmark	Medium
21	1	(Ringsted) – (Fjenneslev)	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Track renewal	16 days and 8 hours		24.05 at 20:00 – 11.06 at 04:00	Single track operations LA80 in adjacent track, LA40 in adjacent track max 400 metres	Banedanmark	Major
22	1	Fjenneslev – (Ringsted)	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Track renewal	11 days		11.06 at 04:00 – 22.06 at 04:00	Single track operations LA80 in adjacent track, LA40 in adjacent track max 400 metres	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
23	1	(Sorø) – Fjenneslev	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Track renewal	5 days		22.06 at 04:00 – 27.06 at 04:00	Single track operations LA80 in adjacent track, LA40 in adjacent track max 400 metres	Banedanmark	Major
24	1	Sorø St.	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Track renewal, extension of track 3 and drainage in Sorø	11 days		27.06 at 04:00 – 08.07 at 04:00	Only operations in Sorø track 1 and 2	Banedanmark	Major
25	1	(Slagelse) – (Sorø)	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Ballast cleaning	4 days and 16 hours		08.07 at 04:00 – 12.07 at 20:00	Single track operations LA80 in adjacent track, LA40 in adjacent track max 400 metres	Banedanmark	Major
26	1	(Ringsted) – Slagelse	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Reconstruction of Sorø and track renewal Fjenneslev Station, track 2.	8 days and 8 hours		12.07 at 20:00 – 21.07 at 04:00	Total closure of lines	Banedanmark	Major
27	1	Sorø St.	NFSP0542 Ringsted – Slagelse speed upgrade and track renewal	Reconstruction of tracks and drainage Sorø. Tracks 1 and 2	21 days		21.07 at 04:00– 11.08 at 04:00	Only operations in track 3 at Sorø St. Tracks 1 and 2 possessed at platform.	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
28	1	(Odense) - Kavslunde	Ny Bane across Vestfyn	Demolition of bridge 20376. Works at traction current system (Kavslunde). Track, earth and drainage works (Odense-Holmstrup)	5 days and 8 hours		16.04 at 20:00 – 22.04 at 04:00	Total closure of lines	Vejdirektoratet/ Banedanmark	High
29	1	(Holmstrup) – (Odense)	Ny Bane across Vestfyn	Earth and drainage works	22 days		22.04 at 04:00 – 13.05 at 04:00	Single track operations LA80 in adjacent track 500m	Vejdirektoratet/Ba nedanmark	High
30	1	(Holmstrup) – (Odense)	Ny Bane across Vestfyn	Track and earth woks	4 days		14.08 – 17.08	Single track operations LA80 in adjacent track 500m	Vejdirektoratet/ Banedanmark	Medium
31	1	(Middelfart) - (Fredericia) / (Taulov)	Snoghøj switches	Renewal of switches	5 days and 8 hours		16.04 at 20:00 – 22.04 at 04:00	Total closure of lines	Banedanmark	Medium
32	1	(Middelfart) - (Fredericia) / (Taulov)	Snoghøj switches	Renewal of switches	5 nights of 12 hours		22.04 at 18:00 – 27.04 at 06:00	Total clouer of lines	Banedanmark	Medium
33	1	(Middelfart) - (Fredericia) / (Taulov)	Snoghøj switches	Renewal of switches	18 days and 22 hours		22.06 at 22:00 – 11.07 at 20:00	Single track operations Middelfart – Snoghøj – Fredericia / Taulov	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
34	1	(Middelfart)-(Fredericia)/(Taulov)	Snoghøj switches	Renewal of switches	2 days and 8 hours		11/7 at 20:00 – 14/7 at 04:00	Total closure of lines	Banedanmark	Medium
35	1	(Middelfart)-(Fredericia)/(Taulov)	Snoghøj switches	Renewal of switches	21 days		14.07 at 04:00 – 04.08 at 04:00	Single track operations Fredericia / Taulov – Snoghøj – Middelfart	Banedanmark	Major
36	1	(Middelfart)-(Fredericia)/(Taulov)	Snoghøj switches	Renewal of switches	15 nights		22.06 – 11.07 14.07 - 04.08	Total closure of lines in Snoghøj 15 nights of 10 hours within the periods	Banedanmark	Major
37	2	Rødby Færge – Nykøbing Falster Vest	Ringsted Femern Banen, Phase II	Extension to two tracks and connection to the Fehmarn Link	Throughout the year		01.01 – 31.12 Until 2029	Total closure of lines excl. Lollandsbanen	Banedanmark	Major
38	2	Nykøbing F – Nykøbing F Vest	RFB - E3006 Ny Kong Frederik IX's bro	Bridge works at new Frederik IX's bridge (mounting af bridge flap)	5 days		09.01 – 13.01	Total closure of lines for Lokaltog between Nykøbing F and Nykøbing F. Vest. Trains from Næstved can come to Nykøbing F. Possessed from mark NF236 til Mrk-NFV214	Banedanmark	Medium

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
39	2	Nykøbing F - Nykøbing F Vest	RFB - E3006 Ny Kong Frederik IX's bro	Bridge works at ny FiX (SAT 2)	3 days		09.05 – 12.05	Total closure of lines for Lokaltog between Nykøbing F and Nykøbing F. Vest. Trains from Næstved can come to Nykøbing F. Possessed from mark NF236 to mark NFV214	Banedanmark	Medium
40	10	København H – Østerport	Drainage works	Drainage works	2 days, 4 hours and 40 minutes		03.01 at 23:40 - 06.01 at 04:20	Total closure of lines Kh-Kk-Kh both main tracks. It will be possible to open 2. main track for DSB approx. every 6 hours for placing of rolling stock.	Banedanmark	Medium
41	11	Københavns Lufthavn Kastrup Station	Ny Kastrup Lufthavn Station	Track works, traction current works platform front edges, bunging	225 days, 2 hours and 30 minutes		02.01 at 04:30 – 15.08 at 07:00	Day possession track 11 and 12 Track 12: SU122 – switch 12(EKSL) Track 11: switch 05 – SU111	Sund og Bælt A/S	High
42	11	Københavns Lufthavn Kastrup Station	Ny Kastrup Lufthavn Station	Final adjustment + mounting of scaffolding for elevators	1 day		29.09 at 04:30 – 30.09 at 04:30	Day possession track 11 and 12 Track 12: SU122 – Switch 12(EKSL) Track 11: switch 05 – SU111	Sund og Bælt A/S	Medium
43	11	Københavns Lufthavn Kastrup Station	Ny Kastrup Lufthavn Station	Dismounting of scaffolding, bridge lifting and mounting of bridge, placement and mounting of staircases and fixed staircases, pergola frames	28 days and 10 hours		16.10 at 07:00 - 13.11 at 17:00	Day possession track 11 and 12 Track 12: SU122 – Switch 12(EKSL) Track 11: switch 05 – SU111	Sund og Bælt A/S	Major
44	11	Kastrup Station, tracks 1 and 2	Signalling Programme	Installation works	4 days		19.09 – 22.09	Tracks 1 and 2 possessed	Banedanmark	Medium

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
45	11	Kastrup Station, track 1 and 2	Signalling Programme	Installation works	4 days		03.10 – 06.10	Tracks 1 and 2 possessed	Banedanmark	Medium
46	11	Kastrup Station, track 11 and 12	Signalling Programme	Installation works	4 days		12.09- 15.09	Tracks 11 and 12 possessed	Banedanmark	Medium
47	11	Kastrup Station	Signalling Programme	Installation works	4 days		05.09- 08.09	Access til klargøringscentret possessed	Banedanmark	Medium
48	11	Peberholm – (Kastrup lufthavn)	Total closure of lines between Sweden and Denmark	Maintenance	2 days		15.03 at 00.01 – 16.03 at 23.59	Total closure of lines	Øresundsbroen	Medium
49	11	Peberholm – (Kastrup lufthavn)	Total closure of lines between Sweden and Denmark	Maintenance	1 day		08.11 at 13:00 – 09.11 at 13:00	Total closure of lines	Øresundsbroen	Medium
50	21	(Odense) – Svendborg	Signalling Programme	Mounting of SP in switches and crossings	9 weekends of 2 days and 8 hours	1. - 2. quarter	01.01 – 30.06	Total closure of lines	Banedanmark	Medium
51	21	(Odense) – Svendborg	Signalling Programme	Placing in service	21 days in the period	3. quarter	01.07 – 30.09	Total closure of lines	Banedanmark	High

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
52	23	(Børkop) - Fredericia	Road access to DSB workshop	Bridge works Børkop-Fredericia	46 days		06.06 – 21.07	Possession of track 9, 302 and 303 Single track operations Børkop – Fredericia, as well as limitations of shunting at Fredericia marshalling yard	Banedanmark	Major
53	23	(Børkop) – Fredericia	Road access to DSB workshop	Bridge works Børkop-Fredericia	3 nights		25.08 – 28.08	Night possessions 11h + 11ht + 9h of track 303, single track operations Børkop – Fredericia, as well as limitations of shunting at Fredericia marshalling yard	Banedanmark	Medium
54	23	(Børkop) - Fredericia	Road access to DSB workshop	Bridge works Børkop-Fredericia	3 nights		26.09 – 29.09	Night possessions 11h + 11t + 9h of track 303, Single track operations Børkop – Fredericia, as well as limitations of shunting at Fredericia marshalling yard	Banedanmark	Medium
55	23	Hørning – Aarhus	Kongsvangbro	Mounting og bung in tracks 40 and 80	2 days and 6 hours		05.12 at 22:00 – 08.12 at 04:00	Single track operations Hørning – Aarhus all trains through track 50 to Aarhus H	Banedanmark	Medium
56	23	(Hørning) - Aarhus	Reconstruction Aarhus H	Platform, bridge and track works	134 days		09.12 2024 – 21.04	Track 6 and track 7 er possessed. No parking at platform	Banedanmark	Major
57	23	(Hørning) - Aarhus	Reconstruction Aarhus H	Platform, bridge and track works	236 days		21.04 - To be continued into TT26	Tracks 4, 5, 6 and 7 possessed + track 40 from switch 02 excl. + track 50 from switch 01 excl. to tracks 4, 5, 6, 7. Only traffic in track 2 and track 3, as well as operations through track 40 / track 40/80 from Hørning	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
58	23/24	Aarhus H	Reconstruction Aarhus H	Track works + Signalling Programme	276 days		24.11 - To be continued into TT26	One track is reconstructed at a time in track group 6xx, 7xx, 8xx, one track is taken out of operation at a time	Banedanmark	Major
59	24	(Brabrand) – Aarhus	Reconstruction Aarhus H	Platform, bridge and track works	134 days		09.12.2024 – 21.04	Track 6 and track 7 are possessed. Parking at platform not possible	Banedanmark	Major
60	24	(Brabrand) – Aarhus	Reconstruction Aarhus H	Platform, bridge and track works	216 days		21.04 - 23.11	Tracks 4, 5, 6 and 7 possessed, Only traffic in track 2 and track 3, as well as operations through track 40 / track 40/80 from Hørning	Banedanmark	Major
61	24	(Brabrand) - Aarhus H	Reconstruction Aarhus H	Platform, bridge and track works + SP	21 days		23.11 – 13.12	Track 4, 5, 6 and 7 possessed, + track 30 from DV signal D301 to I signal I301 + line Brabrand excl. to Aarhus is possessed. Single track operations	Banedanmark	Major
62	25	Frederikshavn – Sindal	Track renewal Kvissel	Track works	2 days and 8 hours		25.07 at 20:00 – 28.07 at 04:00	Total closure of lines	Banedanmark	Medium
63	25	Kvissel Station	Track renewal Kvissel	Track works	20 days, 16 hours		28.07 at 04:00 – 22.08 at 20:00	Either track 1 or track 2 is possessed. No crossing	Banedanmark	High
64	25	Frederikshavn – Sindal	Track renewal Kvissel	Track works	2 days and 8 hours		08.08 at 20:00 11.08 at 04:00	Total closure of lines	Banedanmark	Medium
65	25	Frederikshavn – Sindal	Track renewal Kvissel	Track works	2 days and 8 hours		22.08 at 20:00 – 25.08 at 04:00	Total closure of lines	Banedanmark	Medium

Serial no.	TI B	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
66	26	Tinglev - Padborg	Various rail and welding tasks	Maintenance possessions for welding and rail tasks are integrated and require total closure of lines in Padborg and on the line Padborg - Tinglev	4 days		06.06 – 09.06	Total closure of lines	Banedanmark	Medium
67	29	Esbjerg – (Lunderskov)	Signalling Programme	Placing in service Signalling Programme	11 days, 8 hours		11.04 at 20:00 – 22.04 kl. 04:00	Total closure of lines	Banedanmark	High
68	30	(Ribe) – Tønder Grænse	Signalling Programme	Placing in service Signalling Programme	21 days		21.03 at 20:00 – 11.04 at 20:00	Total closure of lines	Banedanmark	High
69	30	Bramming – Tønder	Signalling Programme	Placing in service Signalling Programme	11 days, 8 hours		11.04 at 20:00 – 22.04 at 04:00	Total closure of lines	Banedanmark	High
70	31	Esbjerg - Spangsbjerg	Signalling Programme	Placing in service Signalling Programme	11 days, 8 hours		11.04 at 20:00 – 22.04 at 04:00	Total closure of lines	Banedanmark	High
71	31	(Holstebro) – (Vemb)	Track renewal Skjern – Holstebro	New tracks in total, exchange of rails and sleepers, ballast cleaning, renovation of passage, etc.	35 days		01.03 – 04.04	Total closure of lines	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
72	31	(Holstebro) – (Skjern)	Track renewal Skjern – Holstebro	Switches and general track renewal at Vemb Station, reisolation bridges across of Tim Stream the stream Storå, start-up of platform renewal Lem Station. SP-placing in service	30 days, 4 hours		05.04 at 00:00 – 04.05 at 04:00	Total closure of lines	Banedanmark	Major
73	31	(Vemb) – (Skjern)	Track renewal Skjern – Holstebro	New tracks in total, exchange of rails and sleepers, ballast cleaning, renovation of passage, etc. Completion of platform works	69 days		05.05 at 04:00 – 14.07 at 04:00	Total closure of lines	Banedanmark	Major
74	31	Holstebro	Establishment of charging points	Mounting of battery chargers	65 days, 4 hours		01.03 at 00:00 – 05.05 at 04:00	Track 2 and track 3 at Holstebro Station possessed. Crossing at Holstebro Station is not possible.	Banedanmark	High

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
75	31	Skjern	Establishment of charging points	Mounting of battery chargers	99 days, 4 hours		05.04 at 00:00 – 14.07 at 04:00	Max 2 tracks at a time can be possessed at Skjern Station. It will always be possible to operate trains from Esbjerg – Skjern-Herning and back. Crossing at Skjern Station is not possible.	Banedanmark	High
76	33	(Aulum) – Holstebro	Track renewal Skjern – Holstebro	New tracks in total, exchange of rails and sleepers, ballast cleaning	52 hours		01.03 at 00:00 – 03.03 at 04:00	Total closure of lines between Aulum and Holstebro. Trains to/from Struer can turn round in track 1	Banedanmark	Medium
77	33	(Aulum) – Holstebro	Track renewal Skjern – Holstebro	New tracks in total, Exchange of rails and sleepers, ballast cleaning	6 nights within the following period		03.03 at 17:00 – 04.05 at 05:00	Total closure of lines between Aulum and Holstebro. Trains to/from Struer can turn round in track 1	Banedanmark	Medium
78	34	Struer - Hvidbjerg	Painting enterprises Oddesund Bridge	Painting and bridge works Oddesund Bridge	4 days		28.03 – 31.03	Total closure of lines	Banedanmark	Medium
79	34	Painting enterprises	Painting enterprises	Painting and bridge works Oddesund Bridge	4 days		13.06 – 16.06	Total closure of lines	Banedanmark	Medium
80	35	(Funder) - (Engesvang)	Funder bakke	Remedy of dam	30 days		05.07 - 03.08	Total closure of lines	Banedanmark	High
81	35	(Funder) – (Silkeborg)	Drainage works	Work due to unstable track	30 days		05.07 – 03.08	Total closure of lines	Banedanmark	High

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
1	820	Bernstorffsvej - Lyngby	NFSP0523 (Sam-Hi)	Track and bridge works Bernstorffsvej - Jægersborg	34 days		13.04 – 16.05	Total closure of lines between Bernstorffsvej and Lyngby incl. Lyngby track 3	Banedanmark	Major
2	820	(Gentofte) - Sorgenfri	NFSP0523 (Sam-Hi)	Track and bridge works Gentofte -Sorgenfri	29 days		16.05 – 13.06	Total closure of lines between Gentofte and Sorgenfri	Banedanmark	Major
3	820	Holte – (Birkerød)	NFSP0523 (Sam-Hi)	Track and bridge works Holte - Birkerød	18 days		14.06 – 01.07	Total closure of lines between Holte and Birkerød	Banedanmark	Major
4	820	Allerød - Hillerød	NFSP0523 (Sam-Hi)	Exchange of switch at Allerød Station	17 days		02.07 – 18.07	Total closure of lines Allerød – Hillerød	Banedanmark	Major
5	820	(Gentofte) - Hellerup – (Svanemøllen)	NFSP0523 (Sam-Hi)	Track and bridge works Hellerup-Gentofte	42 days		18.07 – 28.08	Possession 2. main track Gentofte – Hellerup, Hellerup tracks 5, 6, 7, 8, 15, 16, 60 and 61 and 4. main track Hellerup - Svanemøllen	Banedanmark	Major
6	820	Bernstorffsvej – Gentofte – (Jægersborg)	NFSP0523 (Sam-Hi)	Exchange of switch at Gentofte Station	6 days		28.08 – 02.09	Total closure of lines between Bernstorffsvej and Jægersborg	Banedanmark	Major
7	820	(Svanemøllen) - Hellerup – (Gentofte)	NFSP0523 (Sam-Hi)	Track and bridge works Hellerup-Gentofte	35 days		02.09 – 14.10	Possession 3. main track Svanemøllen – Hellerup, Hellerup tracks 3, 4, 5, 6, 15, 16, 60 and 61 and 1. main track Hellerup - Gentofte	Banedanmark	Major

Serial no.	TIB	Line	Project name	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation cf. Annex II
8	830	(Ballerup) - Veksø	1002901 Kildedal - ny stiunderføring i banedæmning (2019-20943)	Foot path undercrossing	12 days	Summer holidays, week 28 and 29	07.07 – 18.07	Total closure of lines	3.part	Major
9	860	Hellerup - Charlottenlund	NFSP0523 (Sam-Hi)	Track and bridge works Hellerup-Charlottenlund	42 days		18.07 – 28.08	Possession 2. main track Charlottenlund – Hellerup and Hellerup track 5, 6, 7, 8, 15, 16, 60 and 61.	Banedanmark	Major
10	860	Hellerup - Charlottenlund	NFSP0523 (Sam-Hi)	Track and bridge works Hellerup-Charlottenlund	35 days		02.09 – 14.10	Possession Hellerup track 3, 4, 5, 6, 15, 16, 60 and 61 and 3. main track Hellerup - Charlottenlund	Banedanmark	Major
11	880	(Bispebjerg) - Fuglebakken	Renovating of Nørrebro Station	Renewal of access roads and reconstruction	12 days	Easter	11.04 – 22.04	Total closure of lines	DSB Ejendomme	High
12	880	Hellerup – (Lersøen)	NFSP0523 (Sam-Hi)	Track and bridge works in Hellerup	42 days		18.07 – 28.08	Possession Hellerup track 5, 6, 7, 8, 15, 16, 60 and 61 and 2. main track Hellerup - Lersøen		Major
13	880	(Lersøen) - Hellerup	NFSP0523 (Sam-Hi)	Track and bridge works in Hellerup	35 days		02.09 – 14.10	Possession 1. main track Lersøen, Hellerup and Hellerup track 3, 4, 5, 6, 15, 16, 60 and 61 and 3. main track Hellerup - Charlottenlund	Banedanmark	Major
